Sweatshop on P-Chess: the v0.1.0 review, history and home screens

Review screen (REV-005), summary and graph (REV-006), history (HIST-004), delete (HIST-005), analysis queue (HIST-006), home (UI-016), searching (UI-017), your name (UI-018) and profile (UI-019); GPT-6.1 Terra lineup with a Sol fallback, lane `v010`, run 3

Foreman, session `sweatshop/v010/2026-10-30-2302`

31 October 2026

Summary

Run 3 of the `v010` lane in its clone at `.artifacts-build/lanes/v010`, resuming the session of run 2 (PR #28). Bruno was asleep and had given the parent session every call for the night; the parent set the starting decisions (below), the foreman took the routine ones and the proxy the contract one. Launch at 23:29, last merge at 03:15.

- **Produced:** all nine remaining `v010` tickets merged on the session with `Verdict: Approve`: REV-005 (`Review: human`, reviewed tonight by the agent in Bruno's place, as he allowed), REV-006, HIST-004, HIST-005, HIST-006, UI-016, UI-017, UI-018, UI-019. The lane has nothing left. Gate 400 passed, 0 failed (337 before the run).
- **Cost: $20.66** at API list price over 34 stages, all priced: review `gpt-6.1-sol xhigh` $11.49 (15), `gpt-6.1-terra high` $2.70 (9), `gpt-6.1-terra xhigh` $2.70 (5), `gpt-6.1-sol high` $3.09 (4), `gpt-6.1-sol xhigh` implementing $0.68 (1). Codex quota: 6 points of the weekly window (Sol xhigh 4, Terra xhigh 1, Sol high 1, Terra high 0; ±1 each), no reset; 4 Codex rollouts ran outside the stages (the desktop app), 0 points.
- **What went wrong:** Terra high stopped early three times (HIST-004 twice, UI-017 once): one red/green pair, then a progress report instead of a handoff. The foreman's one restart moved HIST-004 to Terra xhigh, which finished it; at UI-017's stop the run switched to the Sol lineup, as authorized. A driver parse defect parked HIST-005's valid handoff once. Six reviews reopened, all real findings.
- **Provisional verdict:** Terra xhigh finishes big tickets (4 of 4 first stage-2 runs to review, 11–12 min); Terra high does not reliably (3 early stops in 7 first attempts). Sol high finished the last three tickets on its first attempt each.

Parent decisions applied before launch: merge `main` (the Godot binding, `1427740`) into the session; REV-005 to `Difficulty: hard` with a comment to resume from run 2's `f5e9337` and finish every criterion; default lineup with an authorized Sol fallback after one diagnosis and restart.

What was done

REV-005: the new review screen. The board, a vertical eval bar, the move list beside it with a class icon on each move once its class is settled, and the engine's best-move arrow. Opening a review runs the Max analysis and fills icons as positions land, reusing a saved analysis when there is one. Partial analysis comes from a new mode in `core/classification.gd` (proxy decision of run 2). Main files `ui/review.gd`, `ui/eval_bar.gd`, `ui/board_view.gd`. Reopened once: with the review open, `F` flipped the hidden game board instead of the review board, and the eval bar did not follow (`ui/review.gd`).

REV-006: the review's summary: accuracy per side, class counts, an interactive eval graph that jumps to a move when clicked, and help tooltips. Main file `ui/review.gd`. Reopened once: the tooltips opened 1241 and 3517 px wide at 800×600, off the window.

HIST-004: the history screen. Tabs (All, wins, losses, draws), game cards with a thumbnail, colours, result and cached accuracy; a card opens its game in the review; the default tab is a setting. Main files `ui/history_screen.gd`, `core/history.gd`. Merged at the first review, which fixed one crash itself: opening History before the first saved game failed on the missing folder.

HIST-005: delete a game, after a confirmation: the PGN and its analysis and snapshot files go, and the result, flag and practice counters are reversed; a failed removal restores files and counts. PGNs gain `PracticeTarget`. Main files `core/history.gd`, `ui/history_screen.gd`. Reopened twice: the rollback repairs had no red/green test (proxy: provoke the failures through the filesystem, no new seam); then, after HIST-006 merged, deleting a game the queue was analysing let the analyser write its JSON back (`ui/history_screen.gd` now cancels the queued analysis).

HIST-006: a background analysis queue, saved across restarts, one game at a time, with priority for the game being reviewed and pause during play; History shows the batch progress. Main files `core/analysis_queue.gd`, `ui/history_screen.gd`. Reopened once: the post-game review ignored a valid saved analysis and started over, and the status lacked "2 of 7".

UI-016: the app opens on a home screen: quick play with the saved choices, Custom game (the old setup screen), History and Settings. Main file `ui/main.gd`. Merged at the first review.

UI-017: a searching screen covers the wait for Maia (at least 0.5 s, until `readyok`) before the game starts; engine failures report there. Main file `ui/main.gd`. Terra high stopped early on it; Sol high implemented it from scratch and it merged at the first review.

UI-018: the app asks your name once and writes it, with `HumanColor`, to every PGN; history and deletion identify you by that colour, and old PGNs fall back as before. Main files `ui/name_dialog.tscn`, `core/pgn.gd`. Reopened once: the name field overlapped the question in the dialog.

UI-019: a profile screen: rename yourself, your results table from the history counters, and a chart of your dated accuracy. Merged at the first review.


Timeline

23:2x	Parent decisions applied: `main` merged into the session (`0a7aa75`); REV-005 hard, resume comment (`d5d14eb`).
23:29	Launch, default lineup (Terra), pid 29940.
23:42	REV-005 to review (Terra xhigh, 12 min, resumed from `f5e9337`).
23:47–23:55	REV-005 reopened (F flips the hidden board), fixed in 4 min, merged.
00:05–00:16	REV-006 to review, reopened (tooltip width), fixed, merged.
00:20–00:21	HIST-004: Terra high stops early, then stops on the recovered commits: blocked.
00:22	Foreman diagnosis, the run's one restart: HIST-004 hard, resume from `2c6272b` (`8ce8bdd`); pid 2204.
00:34–00:40	HIST-004 to review (Terra xhigh, 11 min), merged; the review fixed one crash itself.
00:49–00:57	HIST-005 to review, reopened (no red/green for the rollbacks); the fix asks the proxy (00:54), the proxy decides (00:57).
01:02	HIST-005's fix reaches `to-review`, but the driver parks it (parse defect).
01:13–01:27	HIST-006 to review (Terra xhigh), reopened (cache, batch status), fixed, merged.
01:45–01:52	UI-016 to review (Terra high, 18 min), merged at the first review.
01:54	UI-017: Terra high stops early after 2 min; nothing runnable.
01:55	Foreman: HIST-005's review note reworded (`cc3ee76`), `to-review` restored; UI-017 diagnosis (`8780914`); relaunch on `-Lineup sol`, pid 4876.
02:03	HIST-005 reopened a second time (integration with HIST-006); the driver parks it for diagnosis.
02:18–02:22	UI-017 to review (Sol high, 15 min), merged; nothing runnable.
02:22	Foreman diagnosis of HIST-005 (`476aee7`); relaunch on Sol, pid 29148.
02:32–02:35	HIST-005 to review (Sol xhigh, 9 min), merged.
02:49–03:02	UI-018 to review (Sol high), reopened (dialog overlap), fixed, merged.
03:12–03:15	UI-019 to review (Sol high, 10 min), merged. Nothing left; PR #28 (9 tickets).

Per stage

When	Ticket	Stage	Model	Min	In	Cache	Out	Cost	Outcome
23:42	REV-005	impl	terra xhigh	12	10.4M	99%	24k	0.78	to-review
23:47	REV-005	review	sol xhigh	5	3.8M	94%	18k	0.99	reopened
23:51	REV-005	impl	terra xhigh	4	2.4M	97%	5k	0.21	to-review
23:55	REV-005	review	sol xhigh	4	2.5M	95%	12k	0.62	merged
00:05	REV-006	impl	terra high	10	5.2M	97%	16k	0.50	to-review
00:09	REV-006	review	sol xhigh	4	2.4M	94%	15k	0.67	reopened
00:13	REV-006	impl	terra high	4	1.9M	97%	5k	0.17	to-review
00:16	REV-006	review	sol xhigh	3	1.9M	93%	11k	0.57	merged
00:20	HIST-004	impl	terra high	3	2.1M	95%	4k	0.24	failed
00:21	HIST-004	impl	terra high	1	0.2M	81%	1k	0.05	failed, blocked
00:34	HIST-004	impl	terra xhigh	11	11.0M	99%	26k	0.78	to-review
00:40	HIST-004	review	sol xhigh	7	4.9M	96%	19k	1.03	merged
00:49	HIST-005	impl	terra high	9	5.2M	99%	15k	0.38	to-review
00:53	HIST-005	review	sol xhigh	3	2.2M	92%	11k	0.65	reopened
00:54	HIST-005	impl	terra high	1	0.4M	89%	2k	0.08	asked
01:02	HIST-005	impl	terra high	5	3.3M	98%	8k	0.28	parked*
01:13	HIST-006	impl	terra xhigh	11	9.2M	99%	26k	0.69	to-review
01:19	HIST-006	review	sol xhigh	6	4.2M	95%	22k	1.01	reopened
01:24	HIST-006	impl	terra xhigh	5	2.4M	97%	8k	0.23	to-review
01:27	HIST-006	review	sol xhigh	3	2.0M	93%	10k	0.55	merged
01:45	UI-016	impl	terra high	18	13.1M	99%	26k	0.89	to-review
01:52	UI-016	review	sol xhigh	7	4.4M	96%	17k	0.96	merged
01:54	UI-017	impl	terra high	2	1.1M	96%	7k	0.13	failed, blocked
02:03	HIST-005	review	sol xhigh	6	4.9M	96%	20k	1.05	reopened
02:18	UI-017	impl	sol high	15	5.7M	98%	30k	1.13	to-review
02:21	UI-017	review	sol xhigh	3	3.1M	93%	12k	0.82	merged
02:32	HIST-005	impl	sol xhigh	9	3.5M	97%	15k	0.68	to-review
02:35	HIST-005	review	sol xhigh	4	2.4M	93%	12k	0.66	merged
02:49	UI-018	impl	sol high	14	4.1M	98%	25k	0.84	to-review
02:53	UI-018	review	sol xhigh	4	3.3M	95%	13k	0.77	reopened
02:59	UI-018	impl	sol high	6	2.1M	97%	7k	0.41	to-review
03:02	UI-018	review	sol xhigh	3	1.4M	92%	10k	0.46	merged
03:12	UI-019	impl	sol high	10	3.1M	96%	19k	0.72	to-review
03:15	UI-019	review	sol xhigh	4	2.5M	93%	11k	0.68	merged
				216	132.3M		482k	20.66	

* The run log says `failed (incomplete handoff), blocked`; the stage in fact reached `to-review` with a valid gate receipt (366/0). The driver misread the receipt field (see Driver and runtime issues).

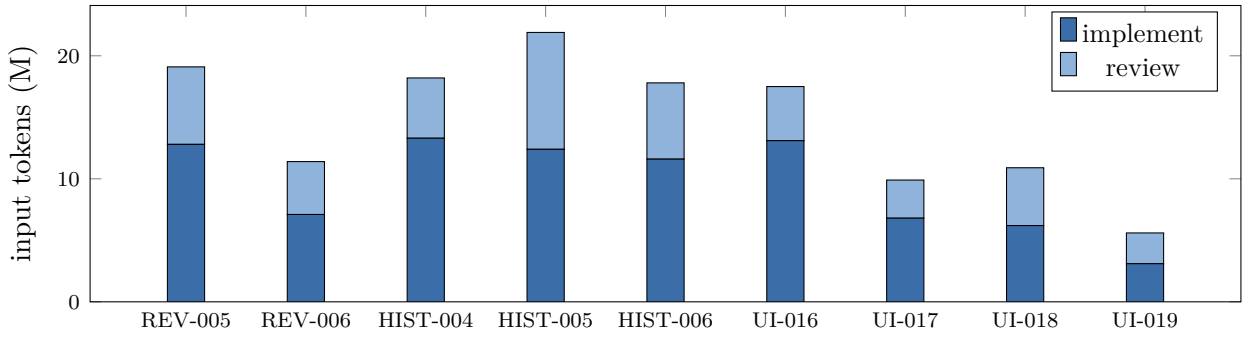

Wasted: the three early stops (HIST-004 2.3M in, $0.28; UI-017 1.1M, $0.13), HIST-005's proxy ask (0.4M, $0.08), and the six rejected first attempts with their reviews. HIST-005's parked fix was not wasted: its work was kept and reviewed. Dollars go mostly to review: $11.49 of $20.66.

Comparison with previous runs

From `run-log.md`. Run 1 of this lane (5 tickets, Terra unpriced) and run 2 (REV-005 only, 4 failed or parked stage 2s, $0.63) set the baseline. Tonight the first stage 2 took 10–18 min on Terra high when it finished (REV-006, HIST-005, UI-016), 11–12 min on Terra xhigh (REV-005, HIST-004, HIST-006), and 10–15 min on Sol high (UI-017, UI-018, UI-019), against Sol high's scoreboard median of 9 min to review. Fixes after a reopen took 4–9 min on every model. Reviews cost $0.46–1.05 ($0.66–1.21 in run 1). Per merged ticket the run cost $2.30.

Observations per model

- **gpt-6.1-terra high, stage 2** (9 stages, 4 tickets): when it finished, it finished well: REV-006, HIST-005 and UI-016 opened with red tests, green gates, honest handoffs. But 3 of its 7 first attempts across runs 2–3 were early stops (HIST-004 after one pair; UI-017 after one test, with uncommitted work), the same failure as REV-005 in run 2. Its second HIST-004 attempt read the recovered commits as work it must not continue and stopped without changes. HIST-005's first handoff carried two rollback fixes without tests. UI-016's quick-play tests wrote eight fake games into the real `user://` history; it noticed, backed them up, removed exactly those eight games and their stats entry, and isolated the test (foreman checked: the 28 real games are intact).
- **gpt-6.1-terra xhigh, stage 2** (5 stages, 3 tickets): every first attempt reached review, on the three largest tickets of the run (REV-005 +533 lines, HIST-004 +560, HIST-006 +471), resuming saved work when told to. Two of three were reopened, each for a regression next to its own change (F flip, cache reuse) plus a stated criterion.
- **gpt-6.1-sol high, stage 2** (4 stages, 3 tickets): three first attempts to review, one reopen (UI-018 layout). On UI-017 it adapted the 14 old tests that the delayed start broke, where Terra had stopped. Slower and dearer per stage than Terra high ($0.72–1.13).
- **gpt-6.1-sol xhigh, review** (15 stages, 3–7 min): every reopen was probed and real; no noise, no drip-feed (HIST-005's second finding came from HIST-006's new code, and the review said so). It fixed one crash itself in HIST-004 with a red/green pair and an independent review. It ran the gate after rebases and reused receipts otherwise.

Driver and runtime issues

1. `GateEvidenceField` (`driver.ps1:214`) takes the first line that matches `Gate evidence:`. HIST-005's round-1 review wrote a bullet "- Gate evidence: reused the supplied receipt..." above stage 2's field, so the driver passed that prose to `Get-Content -LiteralPath ... -Raw`, which failed ("A parameter cannot be found that matches parameter name Raw"), and parked a valid `to-review` as `incomplete handoff`. Once this run; it can recur on any reopen whose review uses that wording.
2. Terra high ends its turn with a progress report on big tickets. The driver counts it as a failed attempt (exit 0, Stage not `to-review`); the second attempt then sees the recovery commits and may stop on them.
3. The Stockfish binary is not in the lane clone, so REV-005, HIST-006 and UI-017 could not exercise the real engine; their handoffs say so.
4. Tests write into the real `user://` folder: `test_*` folders, an analysis JSON from HIST-005's tests and an empty `analysis_queue.cfg` from HIST-006's remain there.
5. Shutdown 0.8–1.8 s per stage; no crash, no timeout, no API error.

Recommendations

1. Fix `GateEvidenceField` to take the last match, or the first whose value is a path that exists; keep the self-check cases at `driver.ps1:822--825`.

2. Do not run Terra high on tickets that span several files and screens: give them `Difficulty: hard` (Terra xhigh) or run Sol high. Implementer rows: `gpt-6.1-terra high` 28 stage runs, 10 failed, 2 asked; `gpt-6.1-terra xhigh` 11 runs, 0 failed; `gpt-6.1-sol high` 68 runs, 0 failed.
3. Make the tests use an isolated user folder throughout (UI-016 did it for its own test), and clean the leftovers in `AppData/Roaming/Godot/app_userdata/[P]Chess`.
4. Put interacting tickets in each other's `Blocked by` (HIST-005 and HIST-006 touch the same analysis files), so the later one is written against the earlier one's code.
5. Before tagging, play the manual checks below with real Stockfish.

Human debt and proxy decisions

No `Débito humano:` lines in this run's tickets. One proxy decision, on HIST-005, asked by the driver after stage 2 stopped on the question:

- `Proxy decided (opus-5.5 xhigh)`: "No new production seam. Stage 2 provokes the failures from the filesystem, the way `tests/test_history.gd:411` already does. The reason: no contract change, it follows the repo's existing pattern, and only `tests/test_history.gd` (a Primary file) changes."

Decisions taken for Bruno without the proxy, by the parent session and the foreman: REV-005 to `hard` with a resume comment; HIST-004 to `hard` with a resume comment; the switch to the Sol lineup at UI-017; REV-005's `Review: human` covered by the agent review tonight.

Reopen attribution

Labelled by the foreman (opus-5.5); the reviewer was `gpt-6.1-sol xhigh`, so no self-judging. Rows appended to `.scratch/reopen-attribution.md`.

Ticket (round)	Finding	Label	Why
REV-005 (1)	`F` flips the hidden game board; the eval bar does not follow	S2-implícito	regression of its own change; the repo already flips with F
REV-006 (1)	Tooltips 1241 and 3517 px wide at 800×600	S2-explícito/ código	criterion 4 names the minimum window; left as manual
HIST-005 (1)	Rollback repairs without red/green proof	S2-explícito/teste	test-first; nothing failed with the repairs reverted
HIST-005 (2)	Deleting a game being analysed lets the analyser rewrite its JSON	S1 ?	the queue merged after HIST-005 was written and reviewed; planning gap, borderline S2
HIST-006 (1)	Post-game review ignores a valid saved analysis	S2-implícito	regression against REV-005's cache reuse
HIST-006 (1)	Status lacks the batch position "2 of 7"	S2-explícito/ código	criterion 3
UI-018 (1)	Name field overlaps the question	S2-explícito/ código	criterion 1; layout untested
HIST-004 (0)	History fails before the first saved game	S2-implícito	fixed in review; failure path of its own screen

Totals, reopens: S2-explícito/código 3, S2-explícito/teste 1, S2-implícito 2, S1 1 (borderline), S3-ruído 0; fixed in review: 1 S2-implícito. No review miss, no review-induced churn, no drip-feed. No session-review, release-audit or post-release finding recorded yet for PR #28.

Scoreboard

`scoreboard.ps1` over the ClassyCall, EasyMath, PhysiSyst, SIGAA-ME and SynchroNice main checkouts plus this lane's clone in place of P-Chess's main checkout (same merged run log; it holds this run's attribution rows before they reach `main`). Moved since run 1's report: implementer

`gpt-6.1-terra high` 10 → 28 stage runs, 1 → 10 failed, 0 → 2 asked; `gpt-6.1-terra xhigh` 1 → 11 runs, 0 failed; pair `gpt-6.1-terra high` → `gpt-6.1-sol xhigh` 9 → 16 reviews, 33% → 31% (S2 rate 31%); `gpt-6.1-terra xhigh` → `gpt-6.1-sol xhigh` 1 → 10 reviews, 30%; `gpt-6.1-sol high` → `gpt-6.1-sol xhigh` 18 → 22 reviews, 22% → 23%. Both Terra pairs now have 10 or more reviews; their reopen rates are about 8 points above Sol high's under the same reviewer. Interventions: automatic-recovery 89 → 101, proxy-decision (opus-5.5 xhigh) 1 → 6 (other lanes included).

Implementer	Stage runs	To review	Failed	Asked	Median min to review	Cost
gpt-6.1-sol high	68	63	0	5	9m	$52.36 (68/68 priced)
opus-5.5 medium	3	2	1	0	6m	$4.79 (3/3 priced)
opus-5.5	7	4	0	3	14m	$15.12 (7/7 priced)
gpt-6-luna max	89	61	10	18	17m	$4.91 (85/89 priced)
sonnet-5.5 high	2	2	0	0	7m	$3.77 (2/2 priced)
gpt-6-astra high	1	0	0	1	-	$3.92 (1/1 priced)
opus-5.5 xhigh	18	14	4	0	12m	$91.78 (18/18 priced)
gpt-6.1-sol max	6	5	0	1	24m	$12.12 (6/6 priced)
gpt-6-sol xhigh	1	1	0	0	9m	$0.40 (1/1 priced)
fable	1	1	0	0	11m	?
gpt-6-luna	8	4	4	0	37m	?
gpt-6-sol	6	5	1	0	17m	?
gpt-5.6-sol	5	4	1	0	17m	?
gpt-6-astra	18	11	6	1	8m	?
sonnet	5	3	2	0	14m	$10.53 (4/5 priced)
sonnet-5 xhigh	11	6	2	3	8m	$18.09 (11/11 priced)
haiku-5.5 high	2	0	2	0	-	$1.00 (2/2 priced)
opus-5.5 high	20	13	6	1	6m	$37.46 (20/20 priced)
gpt-6.1-sol xhigh	10	10	0	0	12m	$10.52 (10/10 priced)
gpt-6.1-terra high	28	16	10	2	8m	$3.49 (14/28 priced)
gpt-6.1-terra xhigh	11	10	0	1	9m	$2.70 (5/11 priced)

Implementer	Reviewer	Reviews	Reopened	Reopen rate	Reopened for S2	S2 rate	Unclassified	Fixed in review for S2
gpt-6.1-sol high	gpt-6.1-sol max	38	12	32%	9	>=24%	2	1
opus-5.5 medium	gpt-6.1-sol max	2	1	50%	0	>=0%	1	0
opus-5.5	opus-5.5	4	0	0%	0	0%	0	0
gpt-6-luna max	opus-5.5 high	18	1	6%	1	6%	0	0
gpt-6-luna max	gpt-6-sol max	43	23	53%	22	51%	0	0
?	gpt-6-sol max	1	0	0%	0	0%	0	0
sonnet-5.5 high	gpt-6-sol max	2	1	50%	1	50%	0	0
opus-5.5 xhigh	gpt-6.1-sol max	6	3	50%	3	50%	0	0
?	gpt-6.1-sol max	1	0	0%	0	0%	0	0
gpt-6.1-sol max	gpt-6.1-sol max	4	1	25%	1	25%	0	0
gpt-6-sol xhigh	gpt-6-astra high	1	0	0%	0	0%	0	0
fable	fable	1	1	100%	0	>=0%	1	0
?	opus	1	0	0%	0	0%	0	0
gpt-6-luna	gpt-6-sol	4	4	100%	0	>=0%	4	0
gpt-6-sol	gpt-5.6-sol	5	4	80%	0	>=0%	4	0
gpt-5.6-sol	gpt-6-astra	4	3	75%	0	>=0%	3	0
gpt-6-astra	gpt-5.6-sol	11	5	45%	0	>=0%	5	0
sonnet	opus	3	1	33%	1	33%	0	0
sonnet-5 xhigh	opus-5.5 xhigh	5	0	0%	0	0%	0	0
?	opus-5.5 xhigh	4	1	25%	1	25%	0	0
opus-5.5 xhigh	opus-5.5 xhigh	7	0	0%	0	0%	0	0
opus-5.5 high	opus-5.5 xhigh	10	2	20%	2	20%	0	3
gpt-6.1-sol high	gpt-6.1-sol xhigh	22	5	23%	5	23%	0	0
gpt-6.1-sol xhigh	gpt-6.1-sol xhigh	10	1	10%	1	10%	0	1
gpt-6.1-terra high	gpt-6.1-sol xhigh	16	5	31%	5	31%	0	0
?	gpt-6.1-sol xhigh	2	1	50%	0	0%	0	0
gpt-6.1-terra xhigh	gpt-6.1-sol xhigh	10	3	30%	3	30%	0	1

Implementer -> Reviewer	Rounds	S2 explicit code	S2 explicit test	S2 implicit	S1	S3 noise
gpt-6-astra medium -> gpt-6.1-sol max	8	11	1	4	1	0
gpt-6.1-sol-fast high -> gpt-6.1-sol-fast max	2	2	0	0	0	0
gpt-6.1-sol-fast max -> gpt-6.1-sol-fast max	6	2	0	3	1	0
gpt-6.1-sol high -> gpt-6.1-sol max	26	16	4	23	1	0
gpt-6-luna max -> opus-5.5 high	1	1	1	0	1	0
gpt-6-luna max -> gpt-6-sol max	23	31	3	23	12	15
sonnet-5.5 high -> gpt-6-sol max	1	3	0	2	0	0
opus-5.5 xhigh -> gpt-6.1-sol max	3	3	0	2	1	0
gpt-6.1-sol max -> gpt-6.1-sol max	5	7	0	5	0	0
haiku-5.5 high -> gpt-6.1-sol max	3	3	1	5	1	0
gpt-6.1-sol high -> gpt-6.1-sol xhigh	54	54	4	23	3	0
gpt-6.1-sol max -> gpt-6.1-sol xhigh	2	0	0	3	0	0
opus-5.5 high -> opus-5.5 xhigh	8	7	0	3	0	0
gpt-6.1-sol xhigh -> gpt-6.1-sol xhigh	3	4	0	1	0	0
opus-5.5 high -> gpt-6.1-sol xhigh	1	2	0	0	0	0
sonnet-5.5 high -> gpt-6.1-sol max	3	5	0	2	3	0
sonnet-5.5 xhigh -> gpt-6.1-sol max	3	7	0	3	2	0
sonnet-5.5 high -> opus-5.5 xhigh	3	1	2	0	0	0
gpt-6-astra medium -> gpt-6-astra xhigh	1	1	0	0	0	0
fable -> ?	4	5	1	3	1	0
sonnet -> ?	10	3	6	9	3	2
opus -> ?	1	3	0	0	0	0
sonnet? -> ?	11	3	4	12	3	5
sonnet -> opus	1	1	1	0	0	0
gpt-6-astra low -> gpt-6.1-sol max	1	2	0	1	0	0
gpt-6.1-terra high -> gpt-6.1-sol xhigh	6	6	1	3	1	0
gpt-6.1-terra xhigh -> gpt-6.1-sol xhigh	4	4	0	3	0	0

Evidence coverage: legacy flags and absent records are unknown, not zero defects or zero interventions.

Discovery	Recorded findings	Earlier review miss (yes / known)	Review-induced churn (yes / known)
ticket-review	383	5 / 188	1 / 190
session-review	30	23 / 25	0 / 29
release-audit	2	2 / 2	0 / 2

Runtime completion to process exit: 314.119s total over 250 measured stages; 334 unmeasured.

Intervention	Recorded events
human-rescue	30
automatic-recovery	101
proxy-decision (unknown)	37
routine-approval	18
proxy-decision (gpt-6-astra high, fallback)	58
proxy-decision (opus)	42
proxy-decision (supervisor)	12
proxy-decision (opus-5.5 xhigh)	6

Pending for the human

1. Review and merge session PR #28 (9 tickets). REV-005 was `Review: human`; the agent review stood in tonight, so read its diff first.
2. Play the v0.0.2 checks with real Stockfish: open a review after a game (icons arrive, eval bar, arrow, `F` flips board and bar, 800×600); the summary, graph clicks and tooltips; History tabs, a card into the review and `Esc` back; delete a game, including one the queue is analysing; queue pause during a game and resume after a restart; home quick play and Custom game; the searching screen; the name dialog on first start and the name in PGNs; the profile rename, table and chart.
3. Fix the driver's `GateEvidenceField` (recommendation 1) and decide Terra high's place in the lineup (recommendation 2).
4. Clean the test leftovers in the real `user://` folder; the eight test games are backed up in `%TEMP%/p-chess-ui016-history-backup` if anything looks missing.
