Sweatshop on P-Chess: the last three open tickets

Release on `v*` tags (CI-003) and two test-harness cleanups (CLEAN-007, CLEAN-008); GPT-6.1 Sol lineup

Foreman, session `sweatshop/2026-10-25-1843`

25 October 2026

Summary

A lane-less run on the main checkout, default lineup `sol` (stage 2 `gpt-6.1-sol high`, stage 3 `gpt-6.1-sol xhigh`). Before launch the proxy (Opus) triaged CLEAN-007 and CLEAN-008 through `grill-proxy` (stage 1), with nothing escalated (`13503f5` on `main`). The first launch at 18:43 was stopped by the foreman after one stage (see *Driver and runtime issues*); the relaunch at 18:50 ended at 19:19 with "Nothing runnable".

- **Produced:** CLEAN-007 and CLEAN-008 merged on the session, both `Review: agent`, `Verdict: Approve`, 0 findings. CI-003 implemented and reviewed with 0 findings, but `blocked`: criterion 5 (a game against Maia from the release ZIP on a clean Windows machine) needs Bruno. Session PR #18; gate 254 passed, 0 failed (253 on `main` before the run); PR CI green on Linux and the Windows export.
- **Cost: $4.18** at API list price over 7 stages: `gpt-6.1-sol xhigh` $2.29 (review), `gpt-6.1-sol high` $1.89 (stage 2). Codex quota: 4 points of the weekly window (`gpt-6.1-sol xhigh` 3, `gpt-6.1-sol high` 1); no thread outside the stages, no window reset.
- **What went wrong:** four local branches left from earlier PRs (pre-rebase copies) made the driver re-review CLEAN-002, already `done`; $0.11 and one revert.
- **Provisional verdict:** cheap and clean ($1.40 per ticket on average, 7–15 min per ticket end to end). The open item is a human playtest, not a defect.

What was done

CLEAN-007: nothing changes for players. Two scene-test harnesses, `tests/test_review.gd` and `tests/test_clock_input_order.gd`, now clean their isolated History folder with the shared `HistoryStorage.clean` instead of a copied loop. No test added or removed; gate count unchanged.

CLEAN-008: nothing changes for players. A test that awaits a signal that never fires now fails after 10 s ("timed out after 10 s") and the run goes on, instead of hanging CI until its 15-minute kill. `tests/run.gd` bounds each awaited test by wall clock; `tests/test_runner.gd` runs its child Godot through a pipe with a 60 s kill. The gate is about 20 s slower (two child runs wait out the bound).


CI-003: pushing a `v*` tag builds the Windows app, downloads Lc0 and the nine Maia nets with their pinned hashes, adds both licences and `THIRD_PARTY.md`, and attaches `P-Chess-windows-x86_64.zip` to a GitHub release named after the tag (`.github/workflows/release.yml`). The test tag `v0.0.1-rc1` produced a public release (99.7 MB). The exported app started on this machine with a fresh profile and launched its bundled Lc0; no game was played (Computer Use refused the window).

Timeline

18:38	Proxy (Opus) triages CLEAN-007 and CLEAN-008; `13503f5` pushed to `main`.
18:43	Launch, pid 28244; session `sweatshop/2026-10-25-1843`. Tree lists CLEAN-002/004/005/006 as `to-review`; CLEAN-002 review starts. Foreman writes `STOP`.
18:44	CLEAN-002 review: already done via PR #11, no change. Driver parks it `blocked` on the session (`98493d4`), opens PR #18, stops.
18:50	Proxy (Opus): rename the four stale branches to `recovery/stale/20261025/*`, revert `98493d4` (`ad20d5d`), relaunch after a dry run. Relaunch, pid 28180.
18:57	CLEAN-007 merged, 0 findings.
19:05	CLEAN-008 merged, 0 findings.
19:14	CI-003 to review; release `v0.0.1-rc1` published by the test tag.
19:19	CI-003 review: 0 findings, `blocked` on criterion 5 (proxy escalated); "Nothing runnable".

Per stage

When	Ticket	Stage	Model	Min	In	Cache	Out	Cost	Outcome
18:44	CLEAN-002	review	sol xhigh	1	0.2M	81%	1k	0.11	to-review (stale)
18:53	CLEAN-007	impl	sol high	3	1.2M	94%	6k	0.43	to-review
18:57	CLEAN-007	review	sol xhigh	4	1.6M	91%	12k	0.69	merged
19:02	CLEAN-008	impl	sol high	5	1.5M	96%	8k	0.48	to-review
19:05	CLEAN-008	review	sol xhigh	3	1.1M	87%	9k	0.57	merged
19:14	CI-003	impl	sol high	10	3.2M	97%	18k	0.98	to-review
19:19	CI-003	review	sol xhigh	5	1.9M	88%	14k	0.91	blocked
				31	10.7M		68k	4.18	

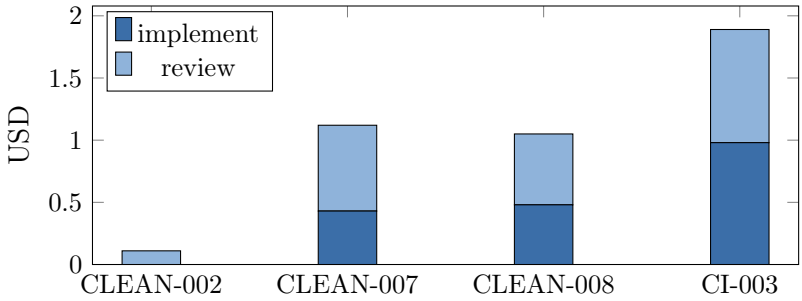

Wasted: the CLEAN-002 review ($0.11, 2.6% of the run), caused by the stale branches.

Comparison with previous runs

From `run-log.md`: the core lane's rework of PR #10 earlier today cost $4.10 for three tickets; this run $4.18 for three tickets plus the stale review. CI-003 is the most expensive ticket of the run ($1.89) because stage 2 waited for a real Actions release and downloaded and re-verified the ZIP.

Observations per model

- **gpt-6.1-sol high, stage 2**: three handoffs at the first attempt, 3–10 min. CLEAN-008 committed its red test before the fix. CI-003 pushed the ticket's test tag and verified the published asset digest, the 19 pinned engine files and a failing package check.
- **gpt-6.1-sol xhigh, review**: three reviews, 0 findings, no code in review (no round-0 rows). Two reviews reused the stage-2 gate receipt instead of rerunning the gate (allowed for unchanged code). The CLEAN-008 review did not discuss the new test's upper bound (child must finish in under 12 s), a possible flake on a slow CI runner; Linux CI passed this time.

Driver and runtime issues

1. The main checkout kept four local branches (`clean-002`, `clean-004`, `clean-005`, `CLEAN-006-main-rematch-lifecycle-tests`) that are pre-rebase copies of PRs #11, #12, #15 and #16: same commits by `git cherry`, different hashes. The driver's `Ticket()` reads `Stage:` from any unmerged branch matching the id unless the session says `blocked`, so the four `done` tickets read as `to-review`. Earlier runs used lane clones, which never had these branches. Not patched; follow-up for the sweatshop skill.
2. `.scratch/run-log/` was missing from the main checkout's `.git/info/exclude`; the foreman added it before launch.

Recommendations

1. Sweatshop driver: treat a ticket branch as merged when the session says `done` and `git cherry <base> <branch>` shows no unique patch.
2. Run foreman lanes in clones, or prune merged-by-rebase local branches before a lane-less run on the main checkout.
3. Keep the `sol` lineup for small tickets: scoreboard row `gpt-6.1-sol high` → `gpt-6.1-sol xhigh`, 18 reviews, 22% reopened, S2 rate 22%.

Human debt and proxy decisions

No `Débito humano:` lines. Proxy decisions of this run:

- **CLEAN-007** (Opus, stage 1): "narrow scope, test_review + test_clock_input_order switch to `HistoryStorage.clean`; helper, test_badges, test_book unchanged"; "no red test" (CLEAN-003 precedent); "do it, low priority (not wontfix)"; "Status ready-for-agent, Stage to-implement, Blocked by none".
- **CLEAN-008** (Opus, stage 1): "10 s wall-clock bound per awaited `test_*`, a constant in run.gd, no CLI flag"; "timeout = FAIL, counted, run continues; the suspended coroutine is abandoned"; "bound `_run` itself in test_runner.gd … waiting synchronously with a kill deadline of about 60 s"; "criteria and Primary files confirmed as drafted".
- **CLEAN-002/004/005/006** (Opus, run anomaly): rename the stale branches, revert `98493d4`, relaunch on the same session.
- **CI-003**: `Proxy escalated (gpt-6-astra high, fallback)` by the review stage: criterion 5 cannot be waived without a clean-Windows game.

Reopen attribution

No reopened review and no fix made in review in this run, so no new rows in `reopen-attribution.md`. No session-review, release-audit or post-release finding was reported since the last pass.

Scoreboard

`scoreboard.ps1` over P-Chess, ClassyCall, EasyMath, PhysiSyst, SIGAA-ME and SynchroNice main checkouts (no lane clone). Rows for this lineup: `gpt-6.1-sol high` → `gpt-6.1-sol xhigh` 18 reviews, 4 reopened (22%), S2 rate 22%; `gpt-6.1-sol xhigh` → `gpt-6.1-sol xhigh` 6 reviews, 1 reopened (an anecdote). The previous report printed 105 reviews for the first pair from a lane clone, whose copied-back log counts rows twice; the two figures do not compare. Interventions: proxy-decision (opus) 30, routine approvals 18, human rescues 24.

Pending for the human

1. CI-003 criterion 5: unzip the `v0.0.1-rc1` ZIP on a clean Windows machine and play one game against Maia; report the Windows version and the result. Then CI-003 returns to `to-review`.
2. Release `v0.0.1-rc1` is public, not marked pre-release and shown as "Latest": keep, mark pre-release, or delete.
3. Review and merge session PR #18 (CLEAN-007, CLEAN-008).
4. The CI-002 note on CI-003 (the missing-engine message points at `scripts/fetch-engine.ps1`, which an export does not ship) was not acted on.
5. The four `recovery/stale/20261025/*` branches can be deleted at your call.
