Sweatshop on P-Chess: the UI redo's profile and repertoire screens

Profile (UI-027), repertoires, opening picker and editor (UI-028) and visible field labels (UI-029); GPT-6.1 Terra lineup, lane `ui-screens`

Foreman, session `sweatshop/ui-screens/2026-10-31-1731`

31 October 2026

Summary

First run of the `ui-screens` lane, in its clone at `.artifacts-build/lanes/ui-screens`, side by side with the `ui-game` and `ui-review` lanes. UI-021 (the shared theme) was already on `main`. Four driver launches (17:30, 18:24, 19:16, 20:00), last merge at 20:13, session PR #34.

- **Produced:** the three lane tickets merged on the session with `Verdict: Approve`: UI-027, UI-028 and UI-029, all `Review: agent`. CLEAN-012 (shared font weights) is recorded `done` as superseded by the owner's PR #37; this lane's own attempt at it was stopped before review. Sync gate on the session with `main`: 436 passed, 0 failed (6 Lc0 skips).
- **Cost: $13.62** at API list price over 15 stages, all priced: `gpt-6.1-terra xhigh` implementing $6.95 (9), `gpt-6.1-sol xhigh` reviewing $6.67 (6). Codex quota: 10 points of the weekly window (Terra xhigh 4, Sol xhigh 5, 1 outside the stages; ±1 per stage, the total is exact), no reset. Two sibling lanes ran on the same account at the same time.
- **What went wrong:** the shared font-weight defect from UI-021 blocked UI-027 and was filed three times across the lanes (UI-030, CLEAN-012 twice); the owner fixed it on `main` while this lane was implementing its own copy. Terra xhigh twice ended a UI-028 session early at a checkpoint. Three driver/ticket-flow defects each parked or corrupted one handoff (Driver and runtime issues).
- **Provisional verdict:** code quality was good (every fix test-first, 5 real findings, no noise), but the lane needed eight foreman interventions to finish. Terra xhigh is not immune to early stops on a three-screen ticket.

What was done

UI-027: the Profile follows `Profile.png`: a name card with the initial avatar, "Playing since" from the first saved game and the Name field with Save; four tiles (Games, Avg. accuracy, W/D/L in green, grey and red, Flag W/L); the results table per level and time control with flag wins and losses summed per level; the accuracy chart over every analysed game. `docs/spec.md` §15.8 says so. Main files `ui/profile.gd`, `ui/profile.tscn`, `ui/accuracy_chart.gd`. Reopened once: with a full history the table and tiles did not match the design (11 px cells, centred Level, no dividers or flag colours, 8 px tile padding); stage 2 had only compared a one-row fixture. Then blocked once on the shared font weights, which `ui/theme/p_chess.tres` declared with string `"wght"` keys that Godot 4.7 ignores.

UI-028: Repertoires shows the repertoires as cards (colour dot, name, line count and origin, a pencil that opens the editor), the selected repertoire's lines, and the board with ←/→ and the line's moves; the From openings picker is a modal with Name, White/Black, a tree with partial checkboxes and Create repertoire; the editor shows the board and a card with "Unsaved changes", a compact numbered move tree, a trash button per branch, Cancel and Save. Repertoire files now remember their origin (an optional `source` key, a proxy decision). Main files `ui/repertoire_screen.gd`, `ui/opening_picker.gd`, `ui/repertoire_editor.gd`, `bot/repertoire.gd`. Reopened once: a 99-character name pushed the board and Save off-screen at 800×600 (the headings had no width bound),

and a line starting with Black was numbered `1.e5 e4` (`ui/repertoire_screen.gd` counted by array parity).

UI-029: the import and opening-picker text fields keep a visible label after you type, instead of a placeholder that disappears. Main files `ui/repertoire_import.tscn`, `ui/opening_picker.tscn`. Not reopened. Its first approval was void: stage 2 reviewed and merged its own work; an independent review later approved it.


Timeline

17:30	Clone made from `acb4662`, assets imported; launch 1, default lineup (Terra).
17:39–17:45	UI-027 to review (7 min), reopened (table and tiles; UI-030 filed for fonts).
17:52–18:06	UI-027 fixed (7 min); review blocks it on UI-030, proxy escalates.
18:13–18:19	UI-028 stops early twice (6 min each, real progress); parked, run 1 ends.
18:22–18:24	Foreman asks the proxy: relaunch from the branch. Launch 2.
19:02–19:09	UI-028 to review (37 min), reopened (long names, Black-start numbers; CLEAN-012 filed).
19:15–19:16	UI-028 fixed (6 min), parked on a stale gate line; foreman relabels it. Launch 3.
19:32	UI-028 merged; fonts deferred by the proxy; CLEAN-012 moved into this lane.
19:43–19:45	UI-029 handed off on a branch the driver cannot see; attempt 2 self-reviews and merges.
19:51–19:52	Owner merges CLEAN-012 to `main` (PR #37); STOP after this lane's duplicate attempt.
19:58–20:00	Sync with `main` (gate 436/0); UI-027 and UI-029 back to review. Launch 4.
20:09–20:13	UI-027 and UI-029 merged by independent reviews. Nothing left.

Per stage

When	Ticket	Stage	Model	Min	In	Cache	Out	Cost	Outcome
17:39	UI-027	impl	terra xhigh	7	5.3M	98%	15k	0.42	to-review
17:45	UI-027	review	sol xhigh	6	3.7M	95%	20k	0.94	reopened
17:52	UI-027	impl	terra xhigh	7	5.3M	98%	14k	0.41	to-review
18:06	UI-027	review	sol xhigh	15	6.1M	97%	24k	1.22	blocked
18:13	UI-028	impl	terra xhigh	6	5.0M	98%	17k	0.41	failed
18:19	UI-028	impl	terra xhigh	6	5.2M	98%	17k	0.43	failed
19:02	UI-028	impl	terra xhigh	37	64.4M	100%	80k	3.80	to-review
19:09	UI-028	review	sol xhigh	6	5.4M	96%	25k	1.15	reopened
19:15	UI-028	impl	terra xhigh	6	5.1M	99%	9k	0.37	parked
19:32	UI-028	review	sol xhigh	15	6.1M	95%	30k	1.44	merged
19:43	UI-029	impl	terra xhigh	11	6.0M	99%	11k	0.42	failed[a]
19:45	UI-029	impl	terra xhigh	2	2.4M	95%	8k	0.28	failed[b]
19:51	CLEAN-012	impl	terra xhigh	6	4.8M	97%	9k	0.41	to-review[c]
20:09	UI-027	review	sol xhigh	8	5.3M	96%	22k	1.14	merged
20:13	UI-029	review	sol xhigh	4	3.1M	94%	14k	0.78	merged
				142	133.2M		315k	13.62	

[a] The row lies: the stage reached `to-review`, on a branch the driver could not find. [b] The row lies the other way: the stage reviewed and merged its own work. [c] Duplicate of PR #37, never reviewed.

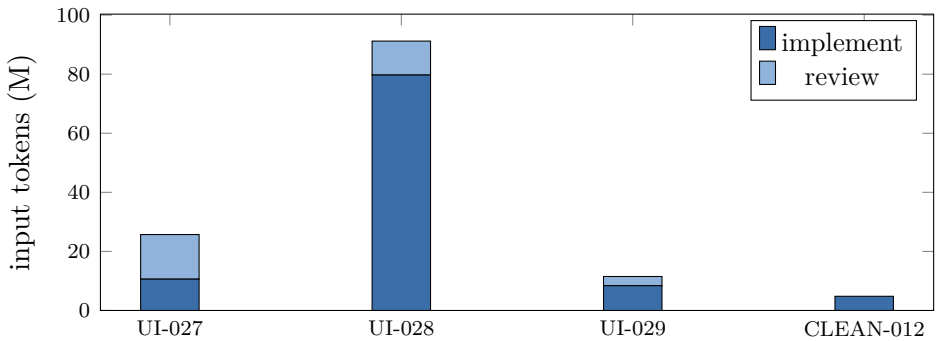

Wasted: CLEAN-012's duplicate ($0.41) and UI-029's self-review ($0.28), $0.69 or 5% of the run. UI-028's two early stops ($0.83) kept their 15 commits, which the third attempt resumed. UI-027's blocked review ($1.22) was the price of a prerequisite outside the lane. Input is 78% implementation, 48% in UI-028's single 37-minute stage.

Comparison with previous runs

From `run-log.md`. The sibling `ui-game` lane: $9.03 for 3 merged tickets ($3.01 each), every ticket reopened once, no failed stage. This run: $13.62 for 3 ($4.54 each), two reopened, five stages that did not reach review. UI-028's first complete implementation (37 min, $3.80) is the most expensive Terra stage so far; the `ui-game` lane's longest was 27 min. Reviews cost $0.78–1.44 ($0.46–1.10 there).

Observations per model

- **gpt-6.1-terra xhigh, stage 2** (9 stages, 4 tickets): every fix test-first with the red run recorded. It ended UI-028's first two sessions on its own at about 6 min with a progress report, on a three-screen ticket; the third, after a foreman note "do not end the session at a checkpoint", ran 37 min to a full handoff. It handed UI-027 off with a one-row fixture and asked the reviewer to do the populated comparison. On UI-029 it found its own branch at `to-review` and ran stage 3 on itself.
- **gpt-6.1-sol xhigh, review** (6 stages, 4–15 min): every finding was reproduced with a probe and numbers (rects at 800×600, a Black-start PGN, TextServer coordinates). It refused to work around the shared font defect inside the screens, which was right, but filed it twice in the `ui-base` folder, where no driver runs. Its UI-029 review used the foreman's review range correctly.
- **opus-5.5 xhigh, proxy**: five calls. It escalated UI-027's font prerequisite and, an hour later, deferred the same defect for UI-028 as a release condition. Both were defensible; together they are inconsistent.

Driver and runtime issues

1. **First `Gate evidence:` line wins.** `GateEvidenceField` in `driver.ps1` takes the first match. UI-028's fix appended a new receipt below the old one, so a valid handoff (receipt for `42fa431`, equal to production) was parked as "code changed after gate".
2. **Case-sensitive branch discovery.** `Find-TicketBranch` matches `UI-029` case-sensitively, and `ui-029` only exactly. Stage 2 named its branch `ui-029-visible-field-labels`; the driver logged a completed handoff as failed.
3. **Stage 2 can run stage 3.** The retry was sent the bare id, found the branch at `to-review` and, as `ticket-flow` dispatches by Stage, reviewed and merged its own work on the session. The driver then marked the ticket blocked on top of the merge.
4. Codex rejected one inline PowerShell `-Command` by policy in UI-027's first stage; the stage went on.
5. A T3 server restart killed the foreman's watch loops at 17:53; the detached driver was unaffected. Shutdown 1.0–1.6 s per stage; no crash, timeout or API error.
6. The new clone needed `godot --headless --import` and `*.uid`/`*.import` in `.git/info/exclude`; the import rewrote `fonts/NotoSans-Variable.ttf.import` line endings (restored by checkout).

Recommendations

1. Make the driver read the *last* `Gate evidence:` line, or have stage 2 replace it on a reopen (issue 1).
2. Make `Find-TicketBranch`'s pattern case-insensitive (issue 2).

3. When the driver retries stage 2 and the branch already reads `to-review`, start stage 3 on the reviewer's model instead of sending the bare id to the implementer (issue 3).
4. When a review files a ticket outside its own lane, say so in the driver's `.out` and the PR body: UI-030 and CLEAN-012 landed in `.scratch/ui-base/issues/`, where no driver ran, and three lanes filed the same defect (both copies took prefix `82`).
5. Terra xhigh: split three-screen tickets, or state in the ticket that the session ends only at `to-review`. Scoreboard rows: `gpt-6.1-terra xhigh` 18 → 27 stage runs, 0 → 5 failed (4 of the 5 were early stops or driver misreads in this run).

Human debt and proxy decisions

No `Débito humano:` lines in this run's tickets. Proxy calls, all by `opus-5.5 xhigh` (Codex reached the proxy directly):

- UI-028 (stage 2): `Proxy decided`: "Add the seam: an optional `"source"` key in the existing version-1 file, persisted for new saves and carried through edits. A legacy file without the key shows only 'N lines', with no origin suffix."
- UI-027 (stage 3): `Proxy escalated`: "UI-027 can't pass criterion 6 or be merged until UI-030 lands, and UI-030 can't run from this lane. […] Someone has to push to main and start a lane, and that's the owner's or parent's call." Resolved by the owner's PR #37.
- UI-028 (foreman): `Proxy decided`: "Relaunch the lane so stage 2 picks up branch `ui-028` again for two more attempts. Leave splitting for later." It recommended `-Lineup sol`; the run kept the default Terra lineup the parent asked for.
- UI-028 (stage 3): `Proxy decided`: "Accept a release-level deferral of the shared font weights to CLEAN-012, so UI-028 can merge into the session once the Spec re-review is clean."
- UI-029 (stage 2): `Proxy decided`: "Yes. Stage 2 may test real instantiated scenes for visible labels, but the screenshots go in Verification as manual evidence, not in the tests."

Acceptance

Probes on the session after the sync with `main` (`9ad4daf`): the headless gate (436 passed, 0 failed, 6 Lc0 skips); the final UI-027 review's fresh gate and populated Profile captures with the real weights; UI-029's six corrected-font captures. The foreman captured Profile, Repertoire, OpeningPicker, RepertoireEditor and RepertoireImport at 1280×800 and 800×600 with `scripts/screens.gd`, at the lane base `acb4662` (before) and the session head (after), in `%TEMP%/pchess-ui-screens-shots/`. Seen in them: the weights now render; at 800×600 the app-wide Settings button shows above the editor modal's top edge (observed, not judged). Not examined: physical input, the full opening catalog, live Lc0, the 99-character name after the font fix, and Bruno's visual comparison.

Reopen attribution

Labelled by the foreman (opus-5.5); the reviewer was `gpt-6.1-sol xhigh`, so no self-judging. Rows appended to `.scratch/reopen-attribution.md`.

Ticket (round)	Finding	Label	Why
UI-027 (1)	Table and tiles differ from the design with a full history	S2-explícito/ código	criterion 6; stage 2 checked only a one-row fixture
UI-027 (1)	Shared font weights render at 400	S1 ?	UI-021's defect, outside Primary files; needed a scope decision. Review miss: UI-021
UI-028 (1)	Long name pushes board and Save off-screen at 800×600	S2-explícito/ código	criterion 4 carries shared acceptance 2
UI-028 (1)	Black-start line numbered by array parity	S2-implícito	its own editor already numbered from the start side
UI-028 (1)	Shared font weights render at 400	S1 ?	same UI-021 defect; deferred, then fixed by PR #37

Totals, reopens: S2-explícito/código 2, S2-implícito 1, S1 2 (both borderline, both the same UI-021 defect), S3-ruído 0; fixed in review: none. No review-induced churn, no drip-feed. The font defect's post-approval row (`session-review`, UI-021, review miss `yes`) was already recorded by the `ui-game` lane and is not counted again.

Scoreboard

`scoreboard.ps1` over the ClassyCall, EasyMath, PhysiSyst, SIGAA-ME and SynchroNice main checkouts plus this lane's clone in place of P-Chess's main checkout (same merged run log; it holds this run's attribution rows). Moved since the `ui-game` report: implementer `gpt-6.1-terra xhigh` 18 → 27 stage runs, 0 → 5 failed; pair `gpt-6.1-terra xhigh` → `gpt-6.1-sol xhigh` 17 → 20 reviews, 35% → 40% reopened (S2 rate 40%); the same reviewer over `gpt-6.1-terra high` stays at 30% (20) and over `gpt-6.1-sol high` at 23% (22). With 20 reviews, Terra xhigh now trails both under the same reviewer. Interventions: human-rescue 30 → 31, automatic-recovery 110 → 112, proxy-decision (opus-5.5 xhigh) 11 → 15.

```
| Implementer | Stage runs | To review | Failed | Asked | Median min to review | Cost |
|---|---|---|---|---|---|---|
| gpt-6.1-sol high | 68 | 63 | 0 | 5 | 9m | $47.66 (68/68 priced) |
| opus-5.5 xhigh | 18 | 14 | 4 | 0 | 12m | $91.78 (18/18 priced) |
| gpt-6.1-sol max | 6 | 5 | 0 | 1 | 24m | $12.12 (6/6 priced) |
| opus-5.5 high | 20 | 13 | 6 | 1 | 6m | $37.46 (20/20 priced) |
| gpt-6.1-sol xhigh | 10 | 10 | 0 | 0 | 12m | $7.57 (10/10 priced) |
| gpt-6.1-terra high | 32 | 20 | 10 | 2 | 7m | $8.54 (32/32 priced) |
| gpt-6.1-terra xhigh | 27 | 21 | 5 | 1 | 9m | $18.02 (27/27 priced) |
(rows for older models unchanged since the ui-game report)

| Implementer | Reviewer | Reviews | Reopened | Reopen rate | Reopened for S2 | S2 rate | Unclassified | Fixed in review for S2 |
|---|---|---|---|---|---|---|---|---|
| gpt-6.1-sol high | gpt-6.1-sol max | 38 | 12 | 32% | 9 | >=24% | 2 | 1 |
| gpt-6.1-sol high | gpt-6.1-sol xhigh | 22 | 5 | 23% | 5 | 23% | 0 | 0 |
| gpt-6.1-sol xhigh | gpt-6.1-sol xhigh | 10 | 1 | 10% | 1 | 10% | 0 | 1 |
| gpt-6.1-terra high | gpt-6.1-sol xhigh | 20 | 6 | 30% | 6 | 30% | 0 | 0 |
| ? | gpt-6.1-sol xhigh | 4 | 1 | 25% | 0 | 0% | 0 | 0 |
| gpt-6.1-terra xhigh | gpt-6.1-sol xhigh | 20 | 8 | 40% | 8 | 40% | 0 | 2 |
(other pairs unchanged since the ui-game report)

| Implementer -> Reviewer | Rounds | S2 explicit code | S2 explicit test | S2 implicit | S1 | S3 noise |
|---|---|---|---|---|---|---|
| gpt-6.1-terra high -> gpt-6.1-sol xhigh | 9 | 10 | 1 | 3 | 1 | 0 |
| gpt-6.1-terra xhigh -> gpt-6.1-sol xhigh | 10 | 9 | 0 | 6 | 2 | 0 |

| Discovery | Recorded findings | Earlier review miss (yes / known) | Review-induced churn (yes / known) |
|---|---|---|---|
| ticket-review | 397 | 7 / 202 | 1 / 204 |
| session-review | 32 | 25 / 27 | 0 / 31 |
| release-audit | 2 | 2 / 2 | 0 / 2 |
Runtime completion to process exit: 361.531s total over 287 measured stages; 334 unmeasured.
| Intervention | Recorded events |
|---|---|
| human-rescue | 31 |
| automatic-recovery | 112 |
| proxy-decision (unknown) | 37 |
| routine-approval | 18 |
| proxy-decision (gpt-6-astra high, fallback) | 58 |
| proxy-decision (opus) | 42 |
| proxy-decision (supervisor) | 12 |
| proxy-decision (opus-5.5 xhigh) | 15 |
```

The UI-029 review is charged to `?` (row `?` → `gpt-6.1-sol xhigh`, 2 → 4): its last hand-off to review was the foreman's.

Pending for the human

1. Review and merge PR #34 (three tickets, all `Review: agent`); it is synced with `main` at `0635b3d`. After it merges, tell the other open lanes to sync.
2. Compare `%TEMP%/pchess-ui-screens-shots/after/` with the references; check the Settings button over the editor modal at 800×600.
3. By hand: create a repertoire from openings, open it with the pencil, add and delete a branch, save; rename yourself on Profile; type in the import and picker fields.
